


## Firewall & Engine Cradle



This picture shows that the two firewall cross tubing pieces have been installed, leveled, and welded in place.

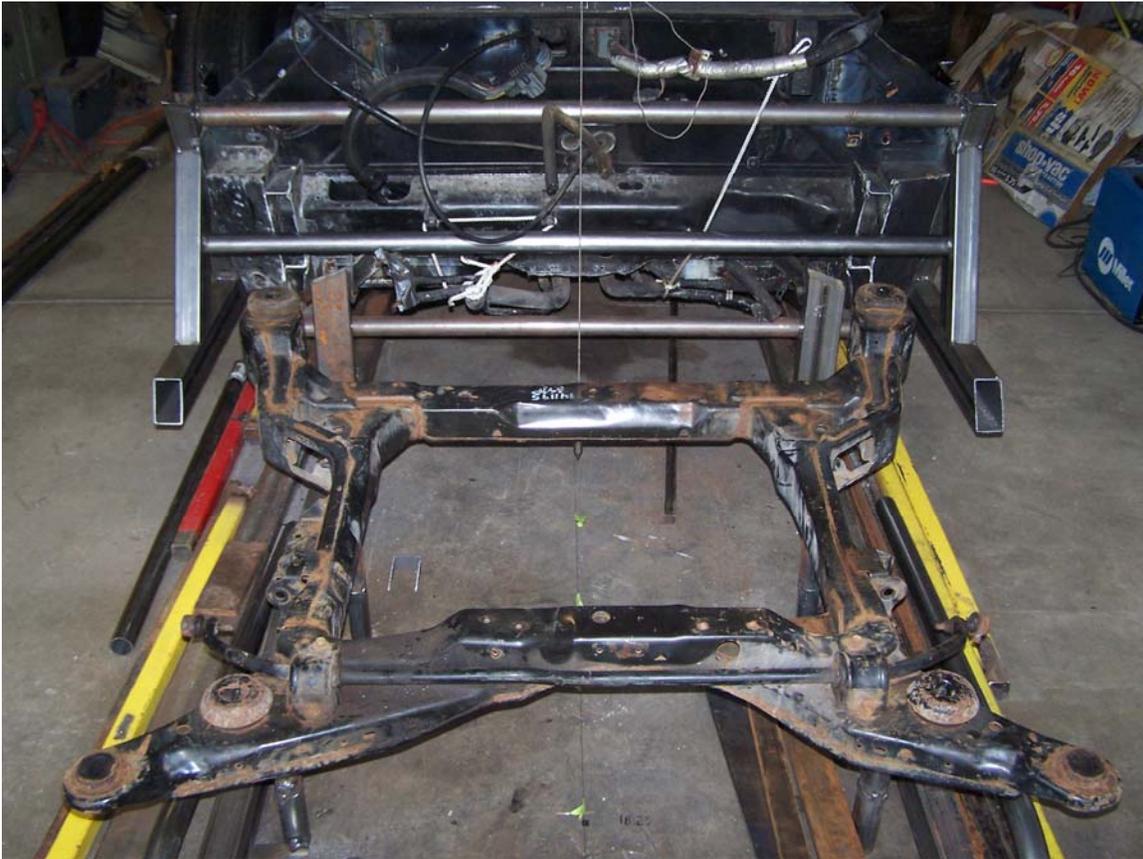

The tubing for the lower hoop has been bent and installed. The four engine cradle attachment brackets are made and welded to the lower tubing hoop. The Cadillac bare block and transmission have been installed to solve clearance problems that may or may not occur. Now I can start on modifying the Cadillac struts to accept coil overs. All measurements at this point are very critical. Measure, measure, measure.
